



Peirce Island WWTf Upgrade Construction

Public Information Meeting

October 21, 2020

Topics of Discussion

- Introductions
- Work Completed Since Last Meeting
- Work to be Completed in Coming Month
- Work Anticipated in Next 6 Months
- Project Construction Costs
- Project Schedule
- Events & Recreation
- Public Input/Comments/Concerns
- Next Meeting



Introductions

- City Staff:

- Terry Desmarais, City Engineer, 603-766-1421
tldesmarais@cityofportsmouth.com


- Website:

<https://www.cityofportsmouth.com/publicworks/wastewater/peirce-island-wastewater-facility/peirce-island-wastewater-facility-upgrade-project>

- News and Updates
- Recreational Info
- Project Info
- Report Form
- Etc.



Areas of Ongoing Construction October 2020

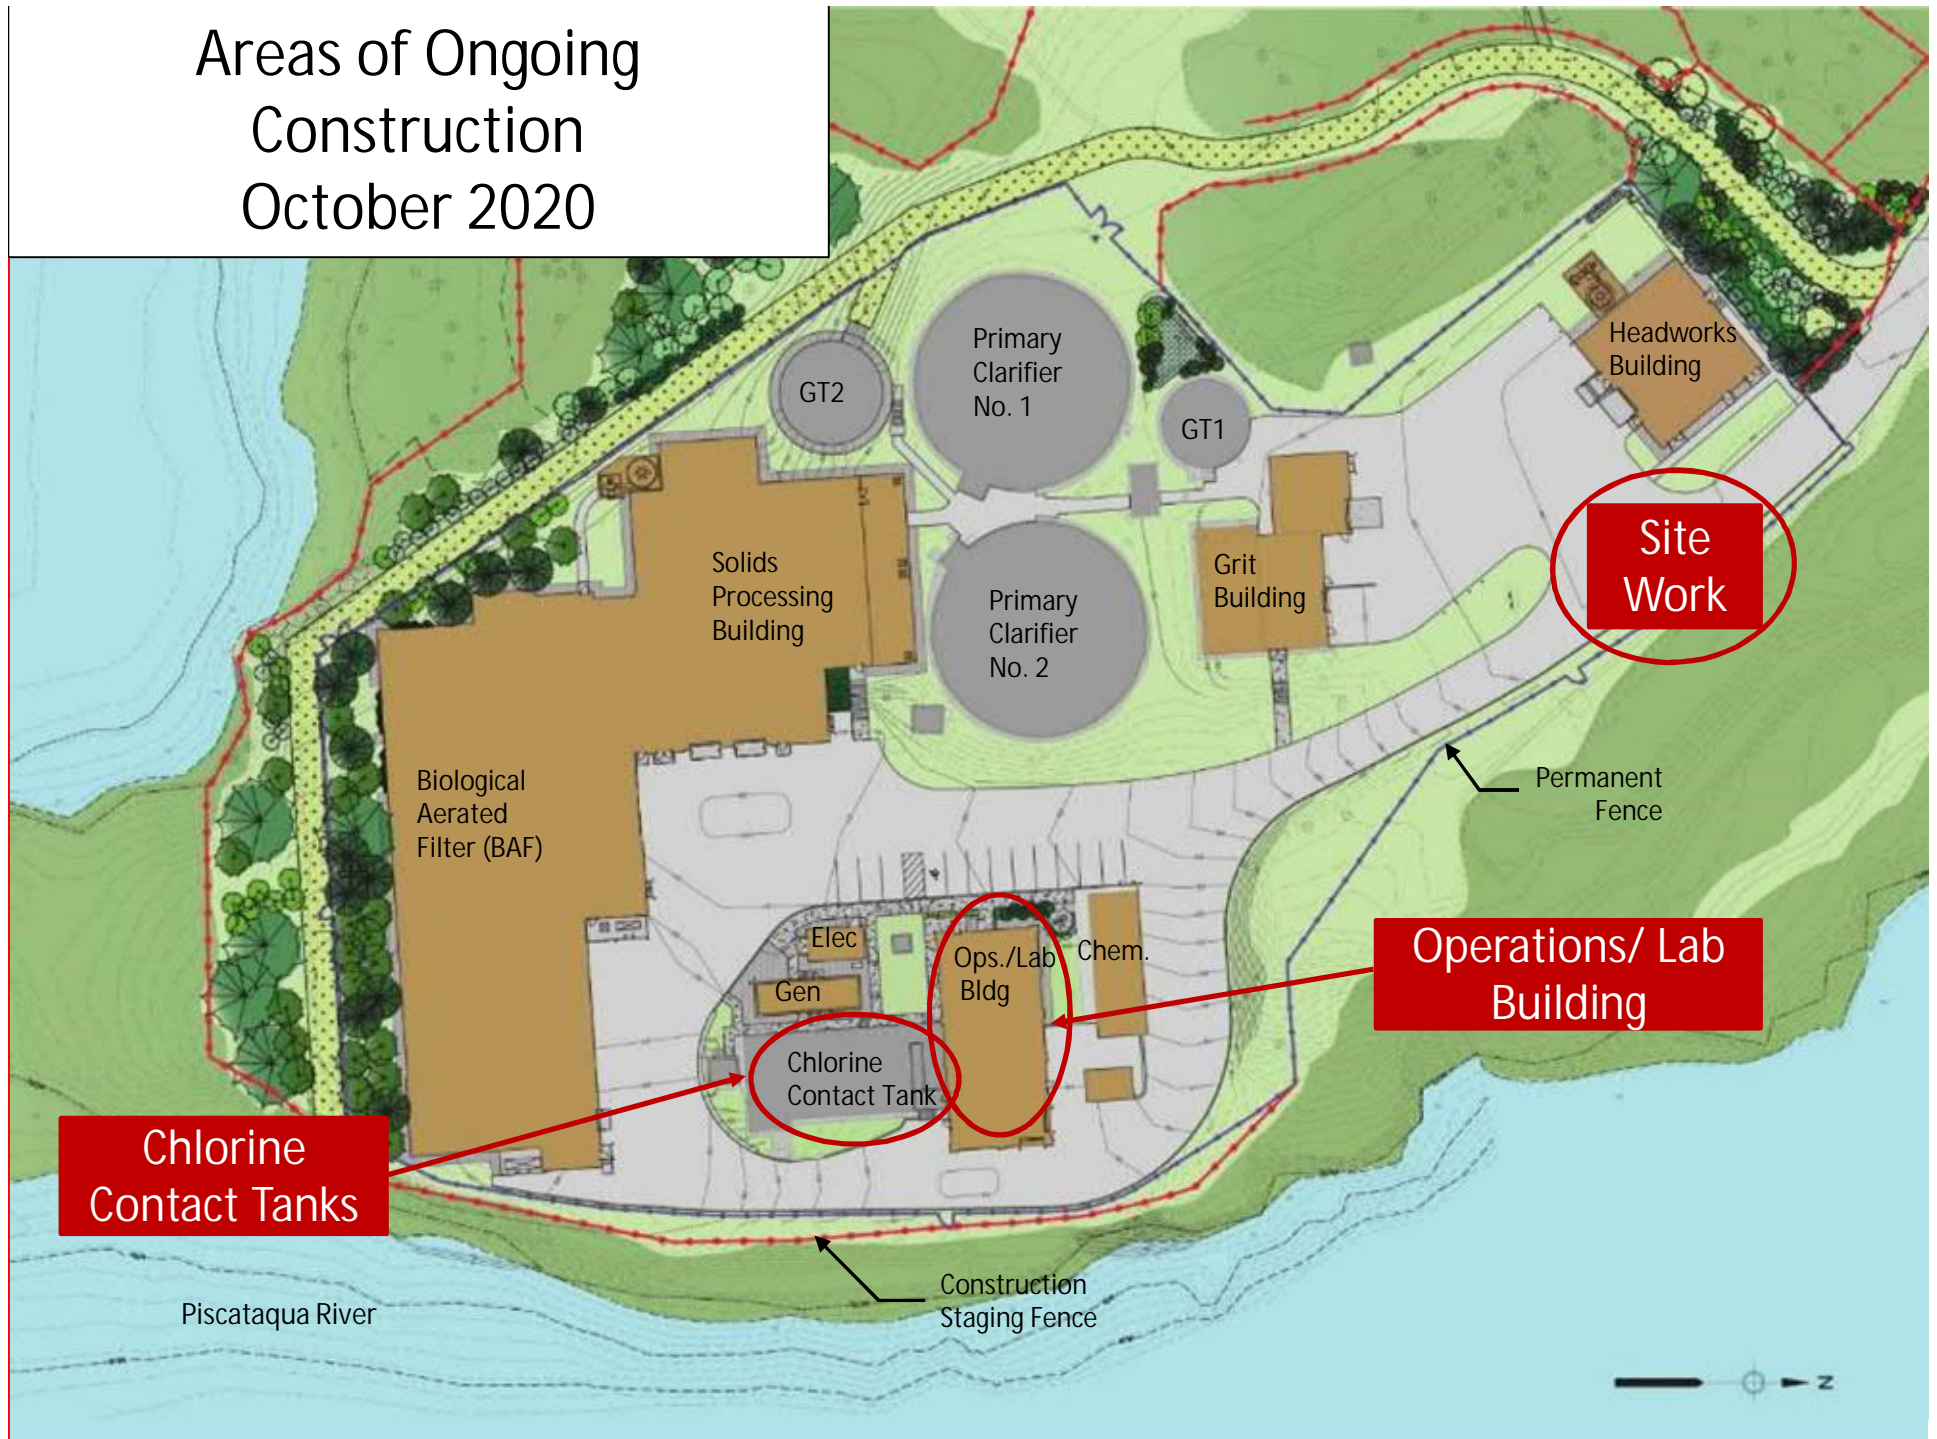

Site Overview November 2016



October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting



Chlorine
Contact Tanks

Site Work

Operations/Lab
Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting



Site Work

October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting



Site Work

October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting



Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting



Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

10

Work Completed Since Last Meeting



Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

11

Work Completed Since Last Meeting



Ops/Lab Building


October 21, 2020



Peirce Island WWTF Upgrade Construction

12

Work Completed Since Last Meeting

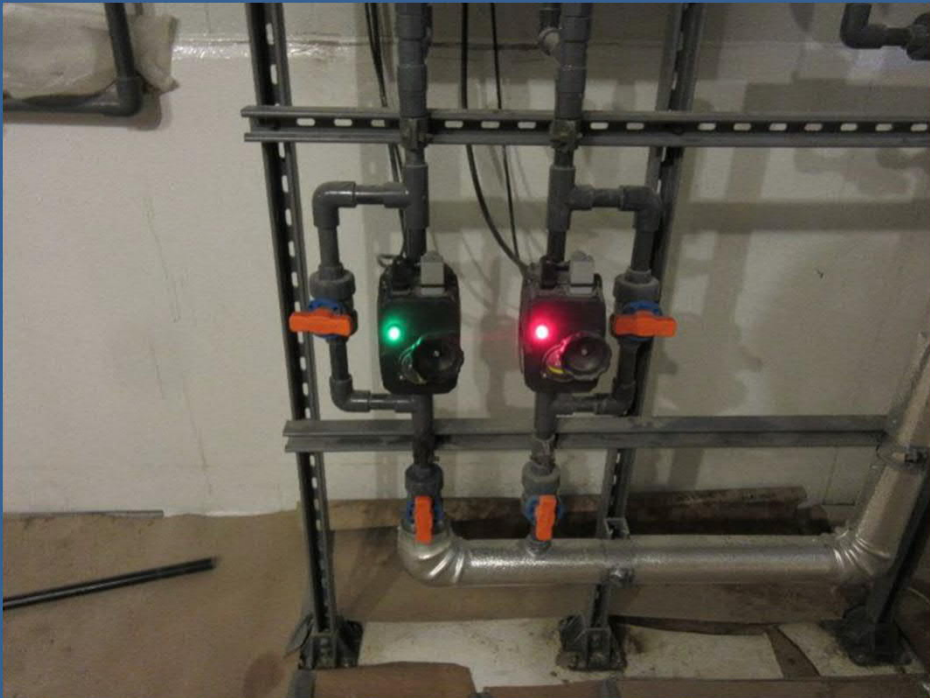

Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

13

Work Completed Since Last Meeting




Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

Work Completed Since Last Meeting

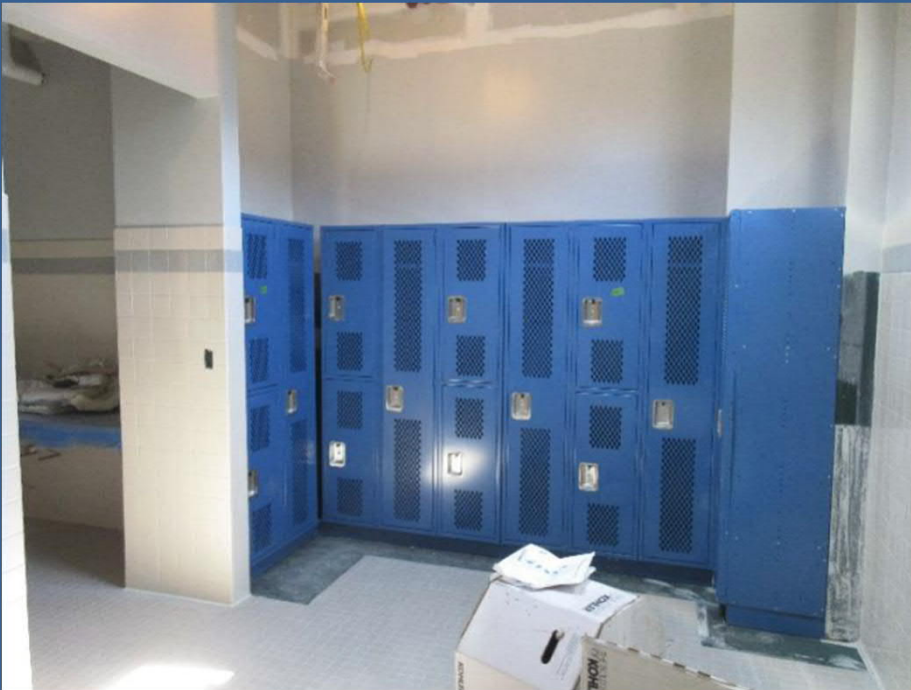

Ops/Lab Building

October 21, 2020



Peirce Island WWTF Upgrade Construction

15

Work Completed Since Last Meeting



Chlorine Contact Tanks

Work to be Completed in Coming Month

- Continue minor finish work at the Headworks Building, Grit Building, Solids Building, and BAF Building
- Continue optimization of the BAF Building process
- Continue integration of the BAF control system with the plant's SCADA system
- Continue installation of the new Operations/Lab Building upper level metal wall façade
- Continue installation of tile and rooftop equipment at the new Operations/Lab Building




Work to be Completed in Coming Month

- Continue installation of laboratory casework, laboratory flooring, and acoustic ceiling tiles at the Operations/Lab Building
- Continue plumbing finish work in the upper level of the Operations/Lab Building
- Continue mechanical process work at the new Operations/Lab Building
- Continue HVAC, electrical, plumbing, and fire protection rough in work at the new Operations /Lab Building
- Continue installation of chain link gates
- Continue site restoration and paving



Anticipated Construction October – April 2021

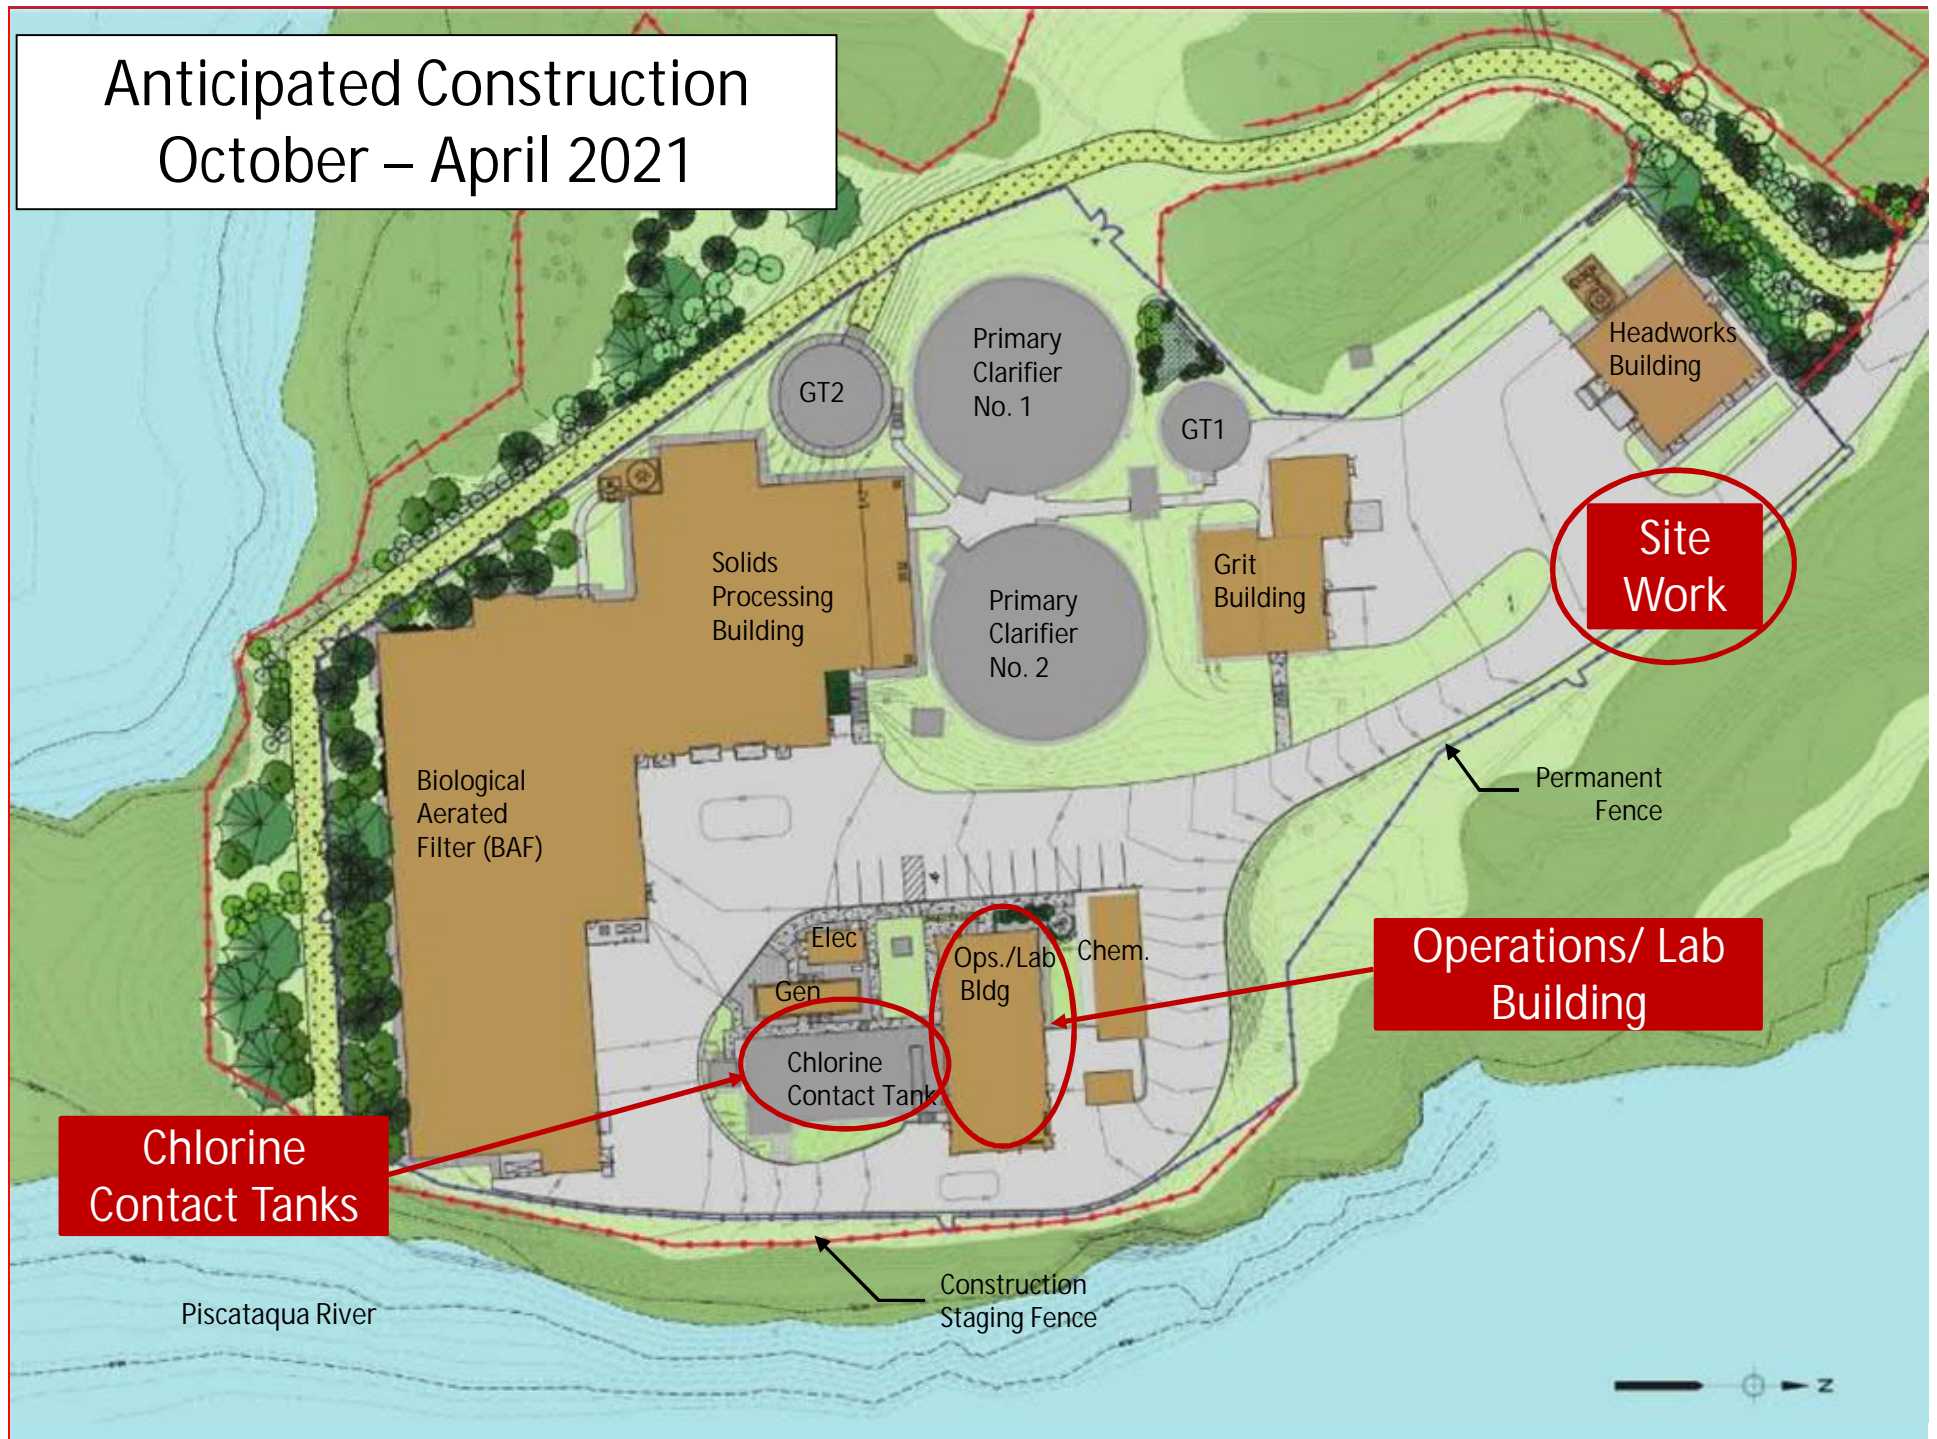

Project Construction Costs


- Original Contract: \$72.786 million
- Change Order No. 1: \$0.367 million
- Change Order No. 2: \$0.547 million
- Change Order No. 3: \$0.093 million
- Change Order No. 4: \$0.163 million
- Change Order No. 5: \$0.250 million
- Change Order No. 6: \$0.292 million
- Change Order No. 7: \$0.169 million
- Change Order No. 8: \$0.113 million
- Change Order No. 9: \$0.242 million
- Change Order No. 10: \$0.123 million
- Total Contract: \$75.145 million




Project Schedule

Milestone	Date	Status
Execute Contract to Construct Upgrades	September 1, 2016	Complete
Submit Two Additional Milestones for EPA Review and Approval	December 1, 2016	Complete
Additional Milestone 1: Transfer of the existing SCADA system to the new Headworks Building	November 21, 2017	Complete
Additional Milestone 2: Startup and testing of the Secondary Influent Pump Station in the new Solids Building	May 9, 2019	Complete
BAF Substantial Completion	December 1, 2019 December 31, 2019	Complete
Achieve Compliance with 2007 NPDES Permit Limits	April 1, 2020	Complete
Achieve Compliance with Consent Decree Total Nitrogen Limits	June 1, 2020	Complete
Project Substantial Completion	June 29, 2020 Tentatively Feb 13, 2021	In Progress
Project Final Completion	September 29, 2020 Tentatively May 22, 2021	In Progress

Effluent Results

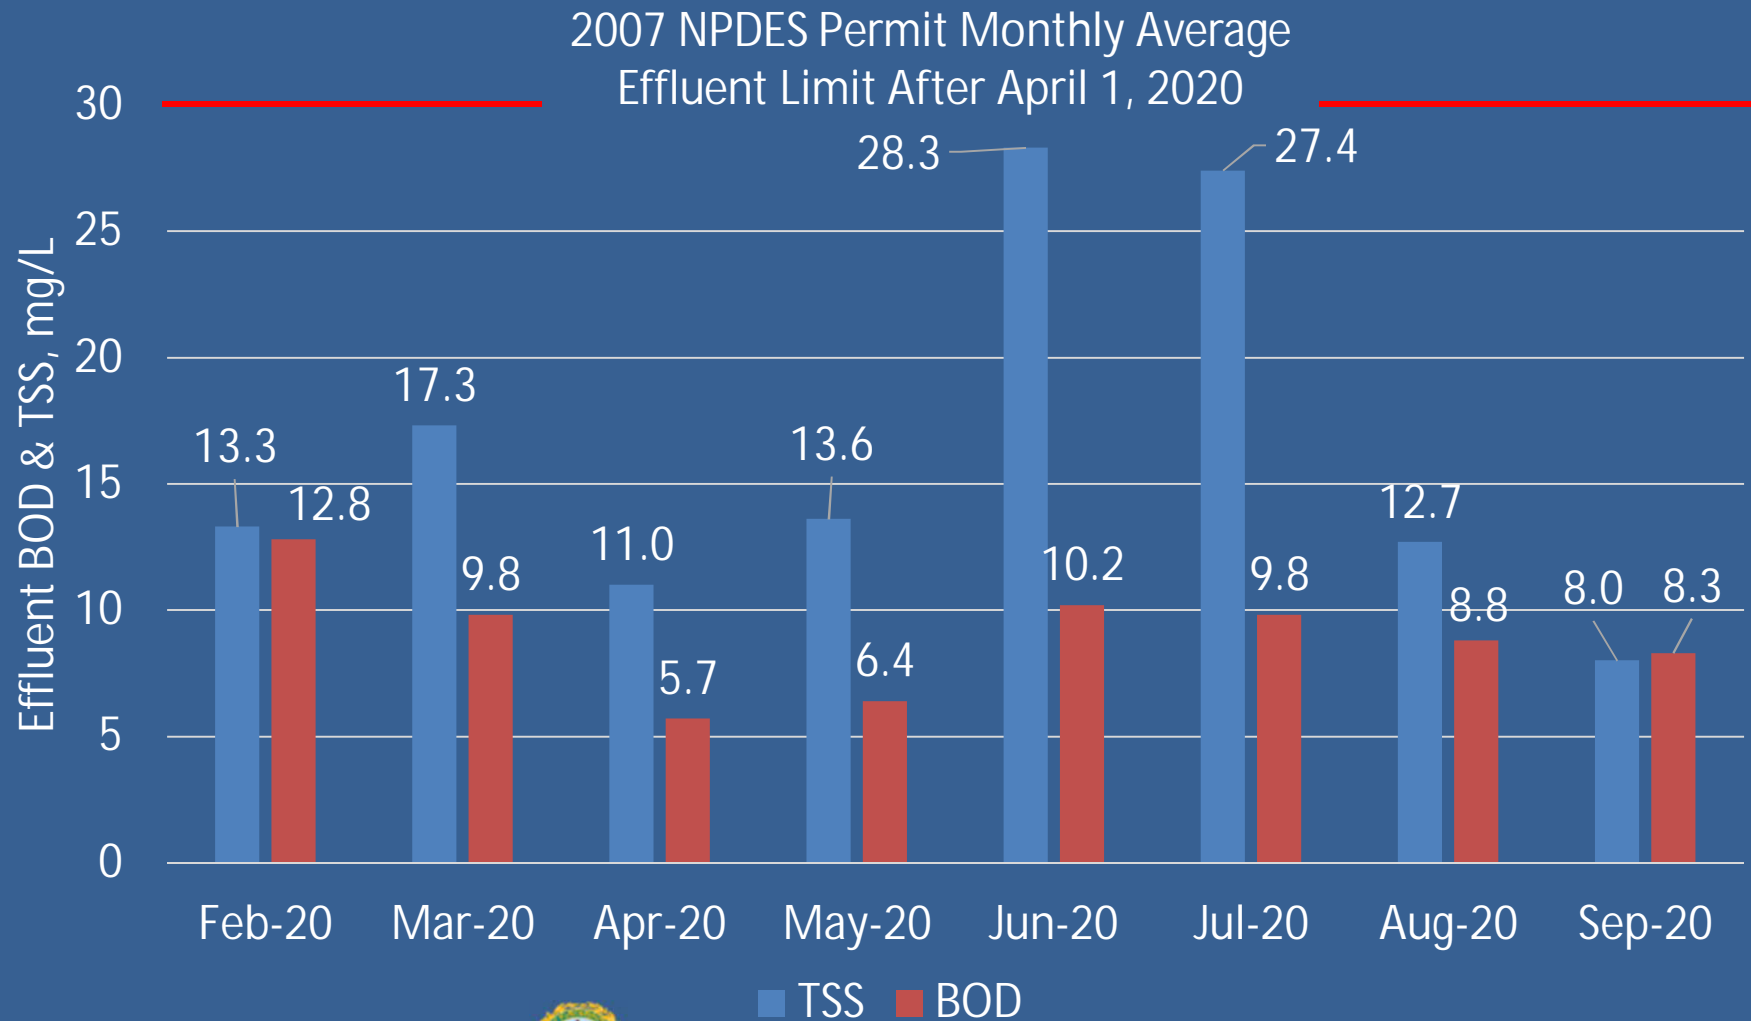

Effluent Results

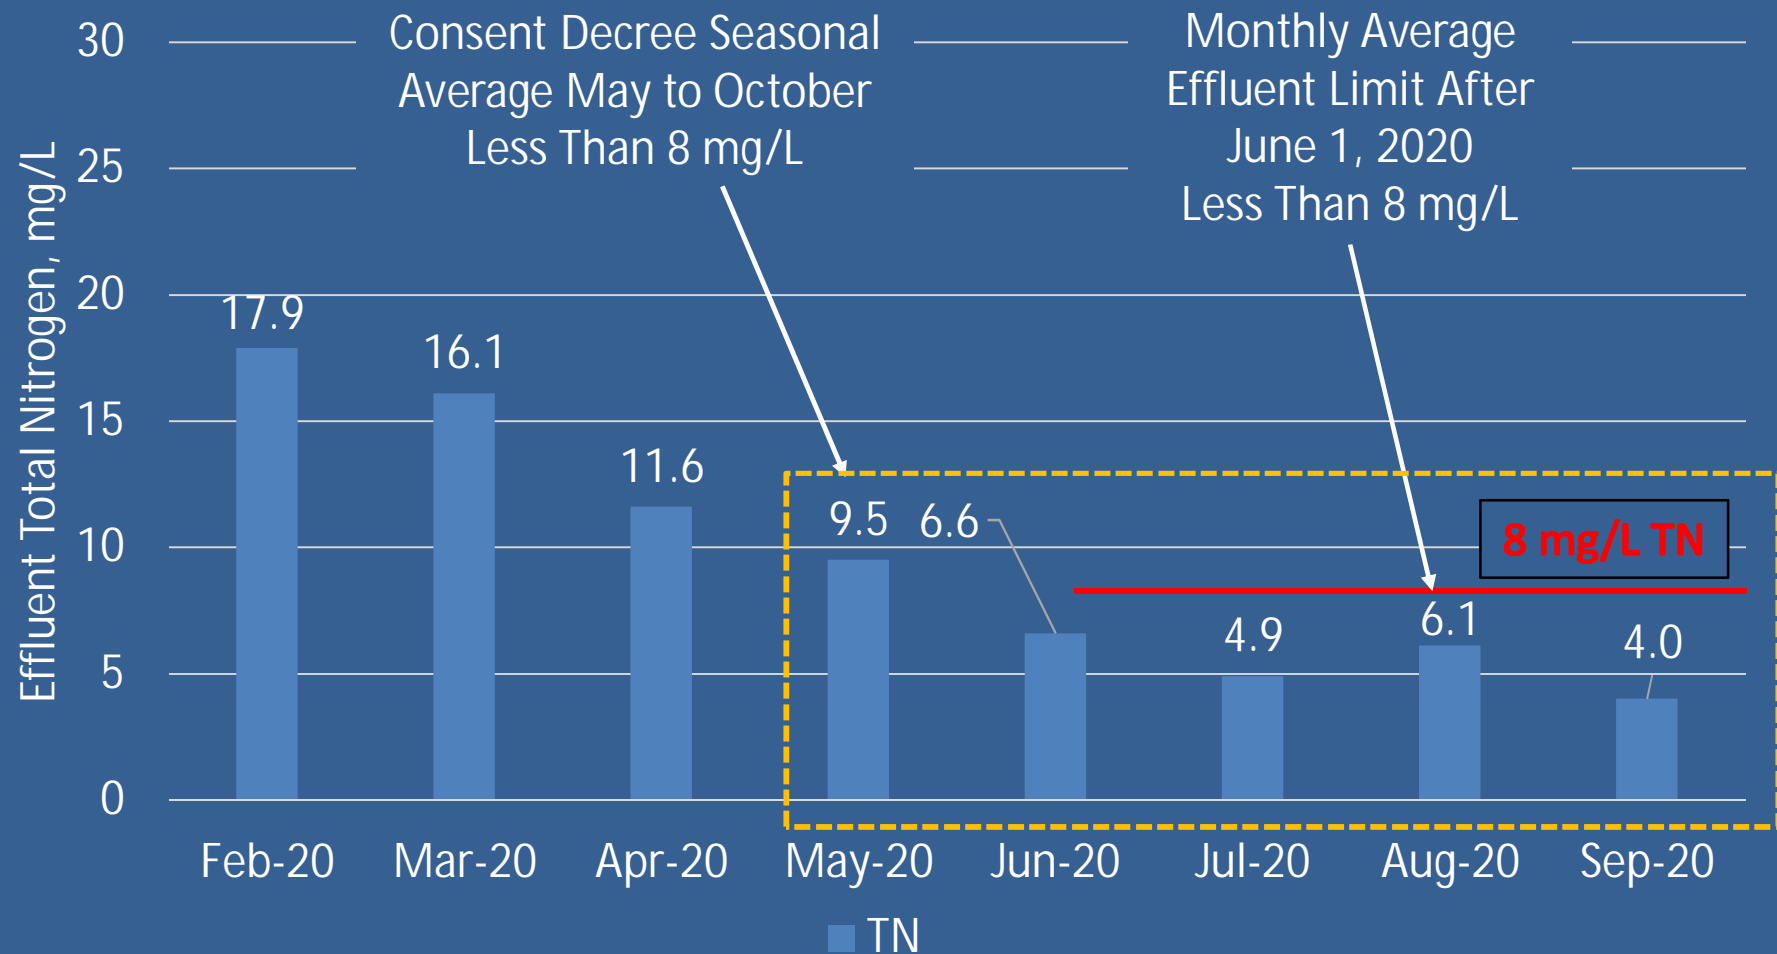


Events and Recreation

- Upcoming
 - No events scheduled.



Force Mains From Mechanic Street Wastewater Pump Station

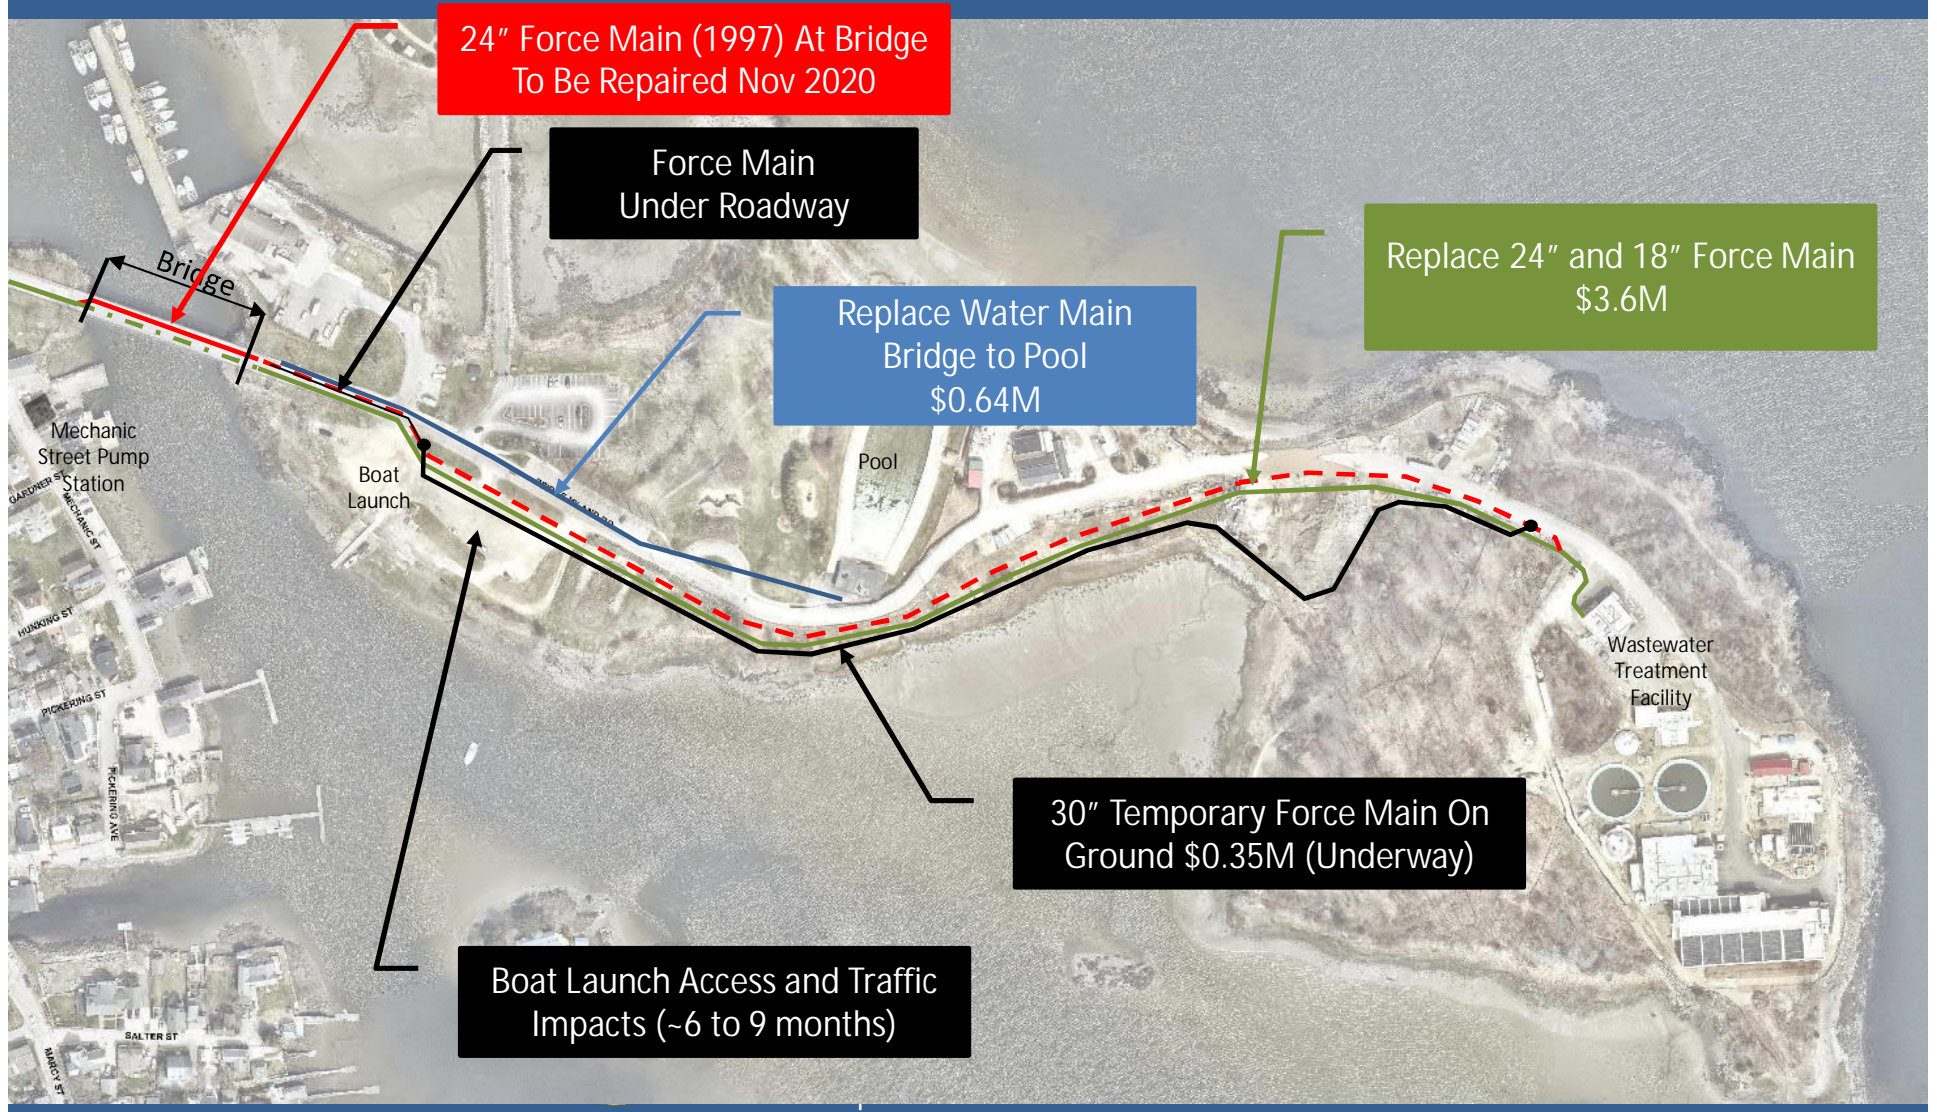



Public Input / Comments / Concerns

Next Meeting

- Public Construction Meeting
 - Next Meeting: November 18, 2020, 11:00 AM

